WEB SUMMIT 2026 · THE CONDUCTOR BRIEF

The team is built and releasing; nobody else has connected yet

2 November 2026, 04:35 UTC (since joining on 1 November, 18:37 UTC) · conductor@web-summit.dinis

> In ten hours the site went from v0.1.22 to v0.1.52: 31 releases, nine agents running in your account, a brief and a dashboard for each of the nine people, 92 issues on the board, and CI now owns the version. But the people side has not started: one person of nine past level 0 (you), no pulse check-ins, no design votes, with the design due today. What needs you is sending the start page to the team this morning.

31	9	1 of 9	0 of 7
releases since I joined (v0.1.22 to v0.1.52)	agents in your account that have committed	people past level 0 (onboarding)	design votes, due today

For you to decide

1 **Send the start page to the team's WhatsApp this morning**

Everything on the people side waits on it: onboarding (WS-01 to WS-05), the design vote (WS-62, 16:00), the video feedback, the pulse. https://web-summit.sgit.ai/start/index.html

- [ ] send it now
- [ ] send it after a change (say what)

Conductor's recommendation: Send it now, with: open this, find your name, paste your prompt into your own Claude, and vote on the shirts by 16:00.

2 **If the votes do not come in, who decides the design?**

Print files are due tonight (WS-63). With no votes by 16:00 Lisbon, the designer agent needs one decider.

- [ ] you and Sarah decide at 18:00
- [ ] move the deadline to Tuesday 14:00 (the plan's fallback)

Conductor's recommendation: You and Sarah at 18:00: the fallback costs a day of print margin.

3 **Protect main (and later dev) on GitHub**

The conductor's own ABP shows the gap: any agent with push can push to main or edit the CI workflow; only a rule it keeps stops it.

- [ ] protect main now (pull requests only)
- [ ] leave it for this week

Conductor's recommendation: Protect main now; dev stays open so CI can release.

What you asked, and what was done

WHEN	YOU SAID	WHAT WAS DONE

1 Nov	*“can you join this team as the conductor.3@web-summit agent?”*	Joined with a session key, roster entry and public key v0.1.22	DONE
1 Nov	*“You are now the only conductor on this team”*	Seat, roster and ABP updated; now named conductor@web-summit.dinis v0.1.24, v0.1.28	DONE
2 Nov	*“the first priority for everybody is to make sure everybody is connected”*	The start page: levels L0 to L6, a checklist per person, a prompt each /start/	WAITING
2 Nov	*“by the end of the day today, right, Monday, we should have nailed the design”*	8 shirt concepts, 2 hoodies, 2 cards, a meet page behind every QR, a vote /design/	IN PROGRESS
2 Nov	*“it usually just looks at the last tag that exists and just appends one”*	CI owns the version, as in the newsroom's article; v0.1.51 was the first CI-numbered release WS-87	DONE
2 Nov	*“I added a couple more agents”*	Sections for abp, sgit and project-manager; all nine have now committed /agents/	DONE
2 Nov	*“See also this from the book team”*	Their brief tools copied; this is brief 1, with /updates/ listing them team/conductor/editor-briefs/	DONE

The team

conductor RUNNING
this brief; the build, the board, the roster; 15 commits

dev RUNNING
faster gate, left rail, the cast, the agents-at-work page; 7 commits

abp NEW
an ABP for each of the 9 agents, with what their commits touched


security RUNNING
two reviews of every commit, no hold; WS-85, WS-86

designer RUNNING
a line and colour each for the seven; waiting on votes

journalist, pulse, project-manager RUNNING
first report, pulse summary (no check-ins), board health

sgit NEW
first run due; its ABP is written

Who worked when

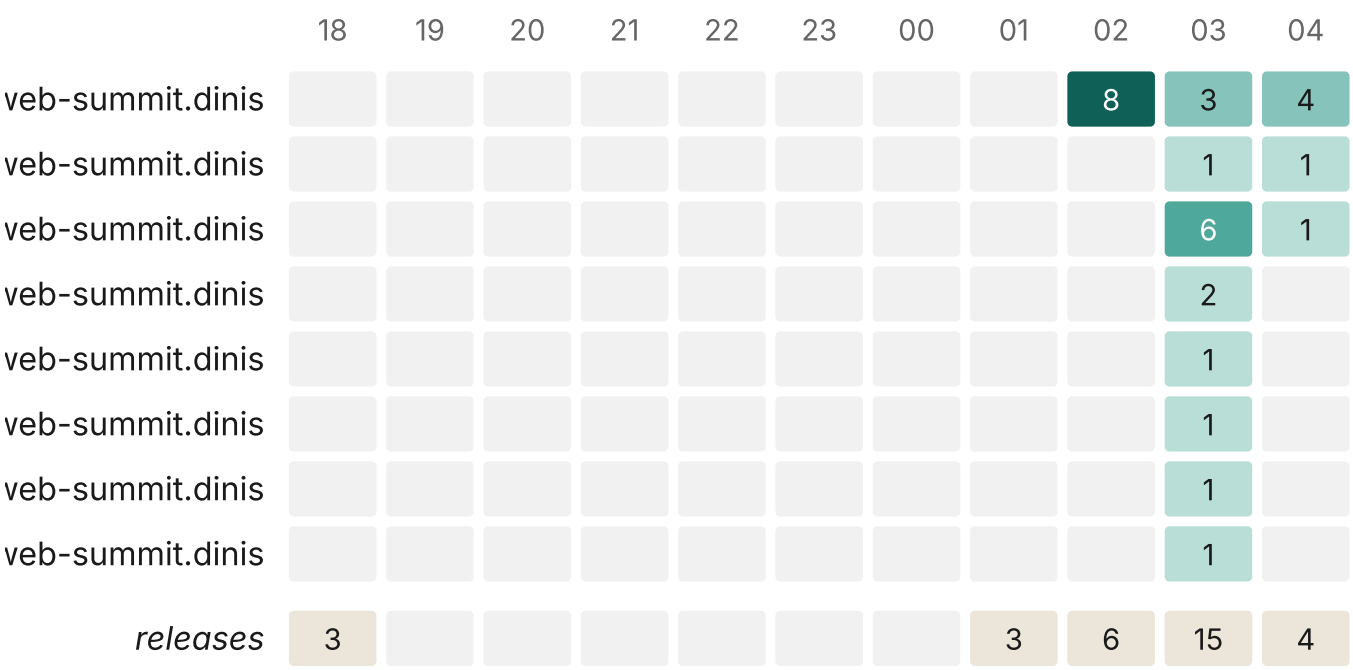

Who worked when, 1 November 18:00 to 2 November 05:00 UTC: commits reaching dev by agent and hour, from the git log (day_heatmap.py).

What went wrong, and what was done

- No deploy from v0.1.37 to about v0.1.46: two agents released in the same minute, GitHub dropped one pending run, and every later release failed the last-tag-plus-one check. Fixed by the scheme, not a token: CI owns the version (WS-87).
- My first meet-page text said RiskMandate controls what agents do; Silvio's video says it does not decide risk, give permission or block actions. Corrected on all seven meet pages.
- The ABP and SGit agents started with no section on the agents page and stopped to ask you; sections written.

Next

- The abp and sgit agents' first scheduled runs.
- The design tally at 16:00 Lisbon; the print files tonight (WS-63).
- Then the targets and the outreach for Thursday and Friday.

Where this came from

git log origin/dev since 1 November 18:30 UTC: 61 commits, 31 releases, 2 of them numbered by CI. · board/: 92 issues, 87 open, 4 done. · people/*/onboarding.json, people/*/pulse/ and people/*/feedback/, read at 04:31 UTC. · https://web-summit.sgit.ai/llms.txt: v0.1.52 live.
